


Housing Reconstruction Status of Barpak Sulikot Rural Municipality

Total Beneficiary: 7,004

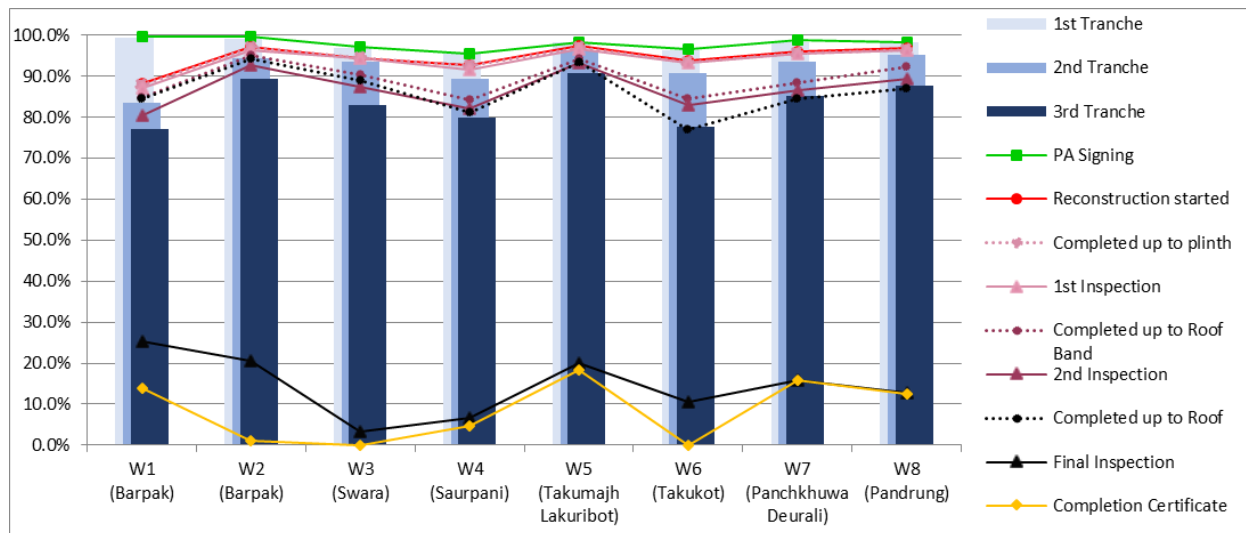

Progress

| Reconstruction Flow | Previous Period | | This Period | | Increase/Decrease | |
|---------------------------|-----------------|-------|-------------|-------|-------------------|-----|
| | % | No | % | No | % | No |
| PA Signing | 97.6% | 6,833 | 97.6% | 6,835 | 0.0% | 2 |
| 1st Tranche | 97.3% | 6,813 | 97.3% | 6,813 | 0.0% | - |
| Reconstruction started | 94.4% | 6,612 | 94.6% | 6,625 | 0.2% | 13 |
| Completed up to plinth | 94.1% | 6,590 | 94.4% | 6,609 | 0.3% | 19 |
| 1st Inspection | 93.4% | 6,539 | 93.9% | 6,576 | 0.5% | 37 |
| 2nd Tranche | 91.4% | 6,404 | 92.1% | 6,452 | 0.7% | 48 |
| Completed up to Roof Band | 88.1% | 6,174 | 88.7% | 6,214 | 0.6% | 40 |
| 2nd Inspection | 85.6% | 5,992 | 86.5% | 6,055 | 0.9% | 63 |
| 3rd Tranche | 83.2% | 5,824 | 83.4% | 5,839 | 0.2% | 15 |
| Completed up to Roof | 85.3% | 5,973 | 85.7% | 5,999 | 0.4% | 26 |
| Final Inspection | 10.4% | 727 | 12.4% | 865 | 2.0% | 138 |
| Completion Certificate | 5.1% | 357 | 6.4% | 451 | 1.3% | 94 |
